


**TRAFFIC CONTROL PLAN**  
**PW VARIOUS LOCATIONS PAVEMENT RENOVATION NO. 54 AND SEWER REPLACEMENT**  
**BASE REPAIR AND GRINDING & PAVING WORK PLAN - 10TH ST FROM MISSION ST TO FOLSOM ST, SF, CA**

Due to the narrow lane width, it is recommended that Contractor delineate travel lanes with temporary tape to minimize maintenance of traffic cones throughout work area.

Submit new plan with lanes delineated with tape if desired.

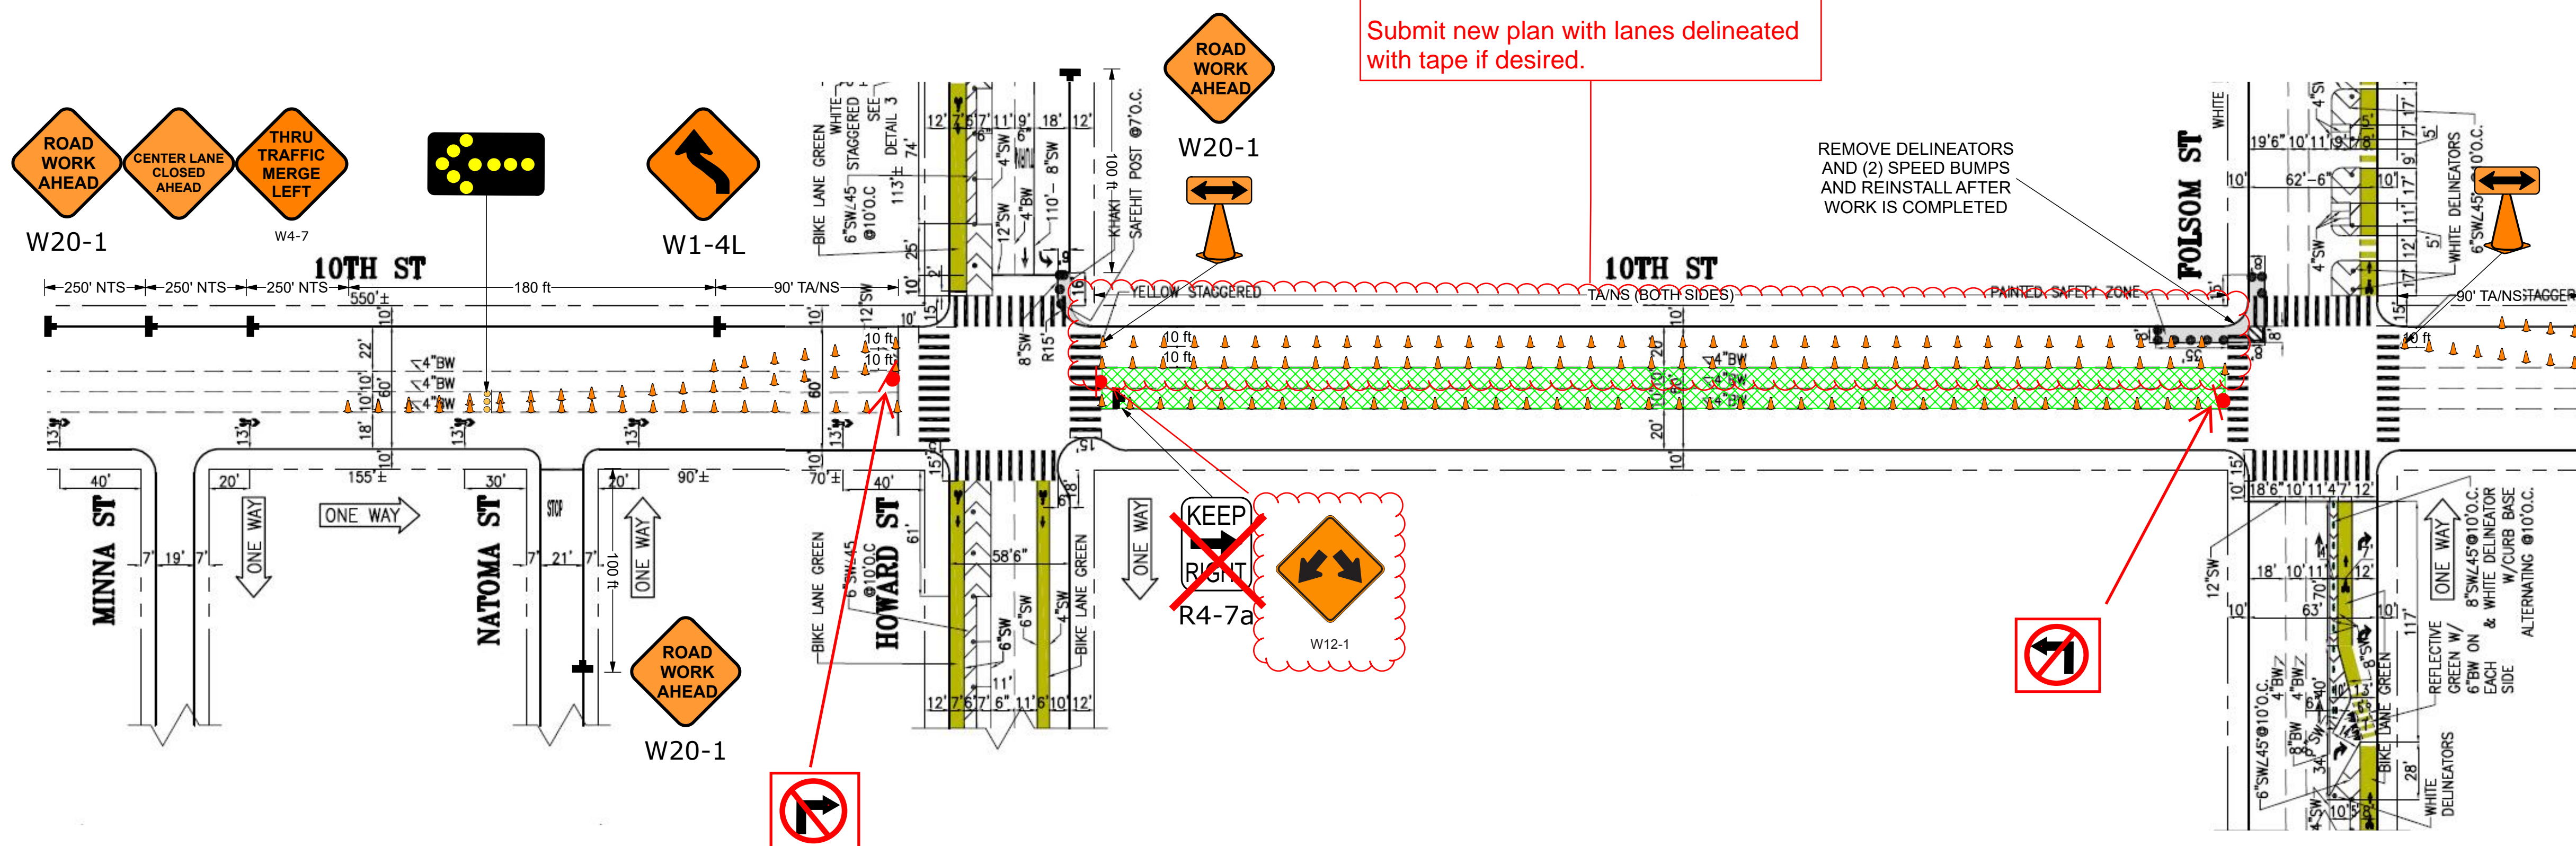

- ☐ NO EXCEPTIONS TAKEN
- ☒ MAKE CORRECTIONS NOTED
- ☐ REJECTED
- ☐ REVISE AND RESUBMIT
- ☐ SUBMIT SPECIFIED ITEM(S)

Review is only for general conformance with the design concept of the project and general compliance with the requirements of the contract documents. Any action shown is subject to the requirements of the plans and specifications. Contractor's responsibilities include, but are not limited to actual dimensions which shall be confirmed and correlated at the job site; preferred fabrication processes and techniques of construction; coordination of the contractor's work with that of all other trades; and the satisfactory performance of the contractor's work.

Sustainable Streets Division  
 San Francisco Municipal Transportation Agency  
 City and County of San Francisco

By [Signature] Date 10/18/2022

Traffic Lane Requirements  
 Number and Width of Lanes

STREET	TIME	NORTHBOUND	SOUTHBOUND	EASTBOUND	WESTBOUND
<b>DURING GRINDING AND PAVING CONSTRUCTION</b>					
10 <sup>TH</sup> Street	9AM – 4PM (M – F) 8AM – 6PM (S/S) At Other Times	-	3@10' 3@10' Full Roadway	-	-
Market, Jessie, Mission, Howard, Folsom, Bryant & Division Streets at 10 <sup>th</sup> Street	At All Times	-	-	Full Roadway	Full Roadway
<b>DURING CONCRETE BASE CONSTRUCTION</b>					
10 <sup>TH</sup> Street *	9AM – 4PM (M – F) 8AM – 6PM (S/S) At Other Times	-	3@10' 3@10' Full Roadway	-	-
Market, Jessie, Mission, Howard, Folsom, Bryant & Division Streets, Natoma St.	9AM – 4PM (M – F) 8AM – 6PM (S/S) At Other Times	-	-	1@10' 1@10' Full Roadway	-

**LEGEND**

	Flashing Arrow Board		Bus Stop
	Flashing Arrow Board (Plan View)		Concrete K-Rail Barrier
	Portable Flashing Beacon		Water Filled Barrier
	Type I Barricade		Not To Scale
	Type III Barricade		Tow-Away/No Stopping
	Type III Barricade (Plan View)		Parking Control / Police Officer
	28" Traffic Cone		Flagger
	Pedestrian Barricade		Equipment
	Work Area		Pipe to be installed
	Sign and Stand		Fixed Mounted Channelizers



3450 3RD ST #30  
 SAN FRANCISCO, CA 94124  
 415-206-1700 PHONE  
 415-206-1711 FAX  
 INFO@CMCTRAFFIC.COM

LICENSE NO 792059  
 GLASS A, 31, C21  
 WBE/SBE/LBE/DBE CERTIFIED  
 WWW.CMCTRAFFIC.COM

Date: 08/03/2022 Author: AM/DD Project: VARIOUS LOCATIONS NO. 54  
 Client: PRECISION Location: SAN FRANCISCO TCP: 038B  
 Job #: 3128 Rev: 0

**Comments:**

- 1) WORK HOURS: SEE TRAFFIC LANE REQUIREMENTS
- 2) CONTRACTOR TO VERIFY EXISTING STRIPING IS ACCURATE PRIOR TO START OF WORK.
- 3) ALL TRAFFIC CONTROL SHALL CONFORM TO THE LATEST EDITION OF THE CA MUTCD.
- 4) ALL TRAFFIC CONTROL DEVICES SHALL BE RETROREFLECTIVE IF SETUP DURING HOURS OF DARKNESS.
- 5) MAINTAIN LOCAL ACCESS TO BUSINESSES AND RESIDENTS AT ALL TIME.
- 6) THE CONTRACTOR SHALL PERFORM THE APPROPRIATE MEASURES TO ENSURE THE SAFETY OF BICYCLISTS ON ALL STREETS ON WHICH THERE IS CONSTRUCTION.
- 7) THE CONTRACTOR SHALL NOT PREVENT OR DELAY THE OPERATION OF MASS TRANSIT VEHICLES AT ANY TIME.
- 8) BASE REPAIR AND GRINDING AND/OR PAVING WORK WILL BE ALLOWED UP TO 2 CONSECUTIVE BLOCKS AND 2 CONSECUTIVE INTERSECTIONS.
- 9) FOR LOCATIONS NOT ADDRESSED IN THE TABLE, CROSS STREETS MAY BE CLOSED FOR UP TO 10 MINS FOR RESIDENTIAL AREAS AND 5 MINS FOR COMMERCIAL AREAS.

